El Segundo High School
Measure M Bond Work
Project Schedule Update 7-9-10
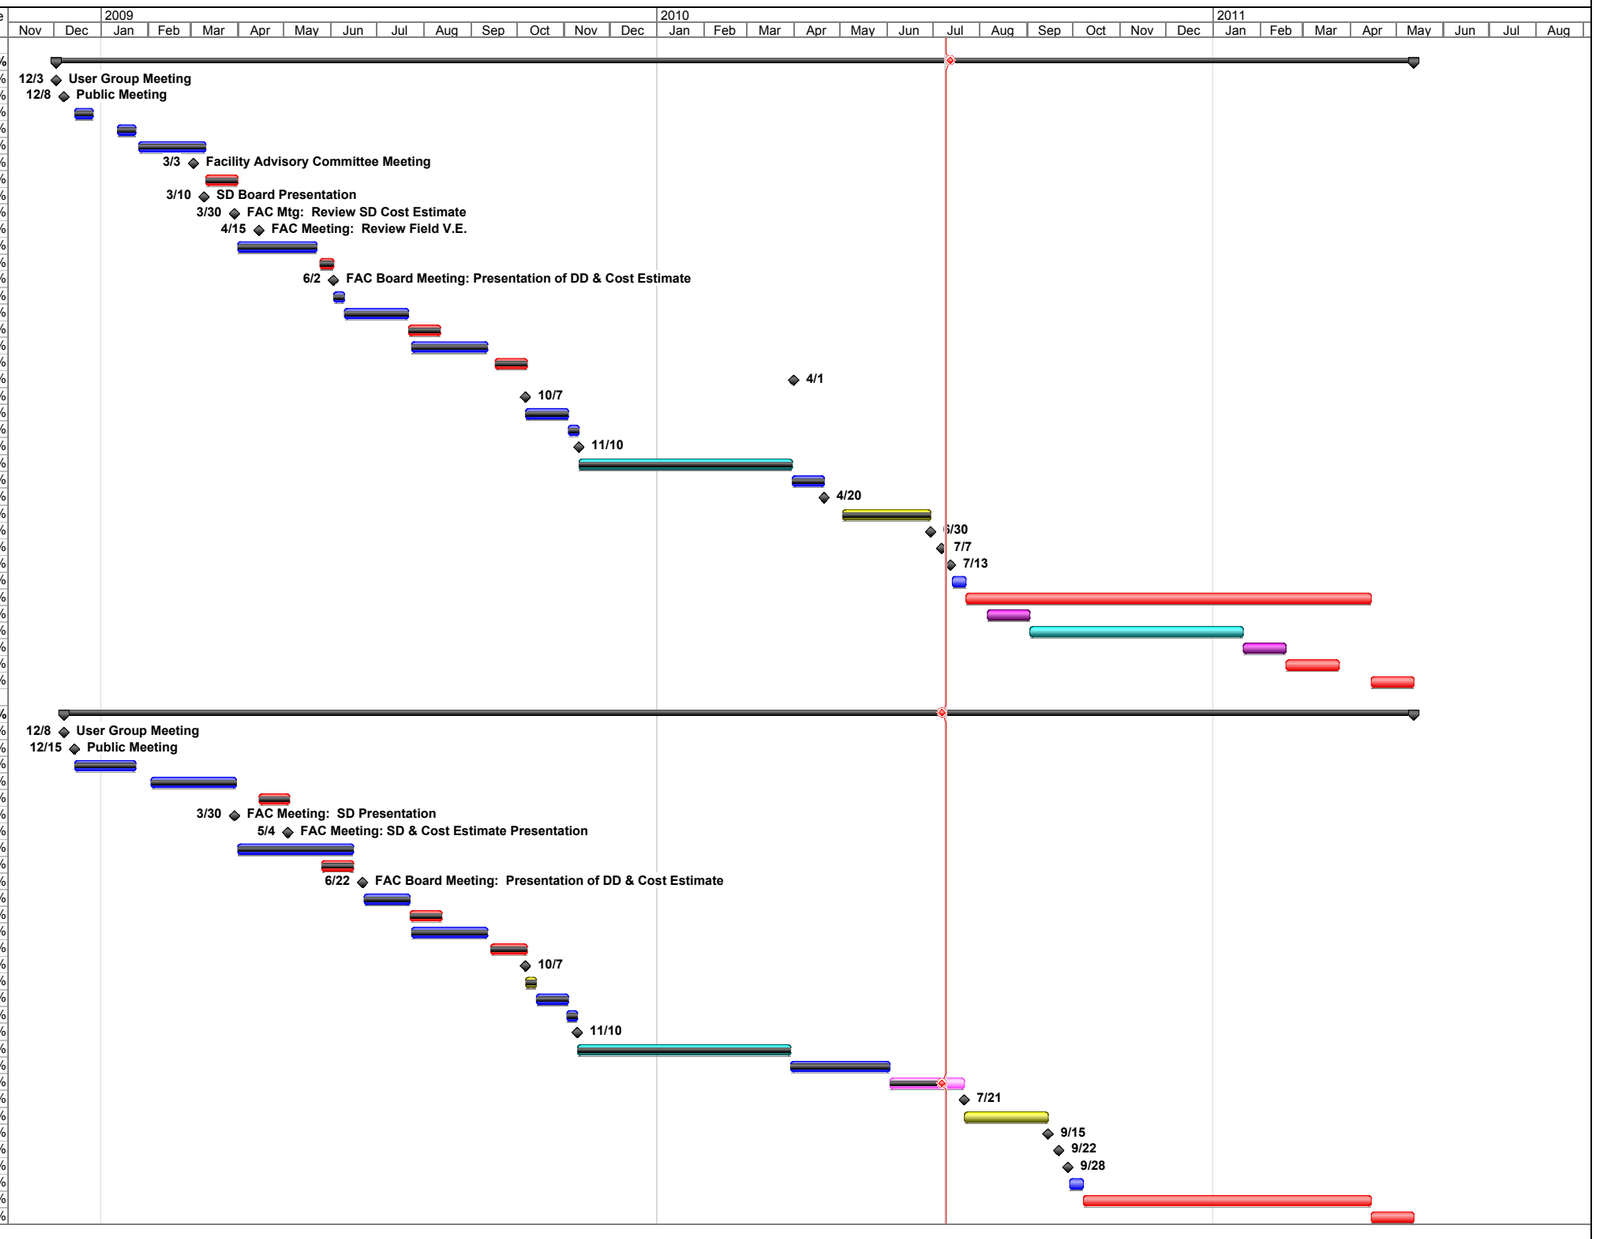
ID	Task Name	Duration	Start	Finish	Predecess	% Complete
1						
2	**Athletic Track & Fields**	**637 days**	**Wed 12/3/08**	**Thu 5/12/11**		**51%**
3	User Group Meeting	0 days	Wed 12/3/08	Wed 12/3/08		100%
4	Public Meeting	0 days	Mon 12/8/08	Mon 12/8/08		100%
5	Master Planning	10 days	Mon 12/15/08	Fri 12/26/08		100%
6	Site Survey	10 days	Mon 1/12/09	Fri 1/23/09		100%
7	Schematic Design	32 days	Mon 1/26/09	Tue 3/10/09		100%
8	Facility Advisory Committee Meeting	0 days	Tue 3/3/09	Tue 3/3/09		100%
9	SD Cost Estimate	15 days	Wed 3/11/09	Tue 3/31/09	7	100%
10	SD Board Presentation	0 days	Tue 3/10/09	Tue 3/10/09		100%
11	FAC Mtg: Review SD Cost Estimate	0 days	Mon 3/30/09	Mon 3/30/09		100%
12	FAC Meeting: Review Field V.E.	0 days	Wed 4/15/09	Wed 4/15/09		100%
13	Design Development	38 days	Wed 4/1/09	Fri 5/22/09		100%
14	Design Development Cost Estimate	7 days	Mon 5/25/09	Tue 6/2/09	13	100%
15	FAC Board Meeting: Presentation of DD & Cost Estimate	0 days	Tue 6/2/09	Tue 6/2/09	14	100%
16	FAC Approval and Notice to Proceed with CD's	5 days	Wed 6/3/09	Tue 6/9/09	15	100%
17	50% CD Set	30 days	Wed 6/10/09	Tue 7/21/09	16	100%
18	50% CD Cost Estimate	15 days	Wed 7/22/09	Tue 8/11/09	17	100%
19	100% CD Pricing Set	36 days	Fri 7/24/09	Fri 9/11/09	17	100%
20	100% CD Cost Estimate by CW Driver	15 days	Thu 9/17/09	Wed 10/7/09	19	100%
21	Submit Geotechnical Report to CGS	0 days	Thu 4/1/10	Thu 4/1/10		100%
22	FAC Board Meeting to Review 100% CD Set	0 days	Wed 10/7/09	Wed 10/7/09		100%
23	Incorporate District Comments/Changes	20 days	Wed 10/7/09	Tue 11/3/09	22	100%
24	Prepare DSA Submittal Package	5 days	Wed 11/4/09	Tue 11/10/09	23	100%
25	**DSA Submittal**	**0 days**	**Tue 11/10/09**	**Tue 11/10/09**	24	100%
26	DSA Review	100 days	Wed 11/11/09	Tue 3/30/10	25	100%
27	DSA Corrections & Resubmittal	15 days	Wed 3/31/10	Tue 4/20/10	26	100%
28	**DSA Approval (estimated)**	**0 days**	**Tue 4/20/10**	**Tue 4/20/10**	27	100%
29	Bidding & Negotiation	42 days	Mon 5/3/10	Tue 6/29/10	28	100%
30	FAC Small Group meeting to review GMP	1 day	Wed 6/30/10	Wed 6/30/10	29	100%
31	FAC meeting to issue GMP Recommendation to BOE	1 day	Wed 7/7/10	Wed 7/7/10	30	100%
32	Board of Education Meeting to approve GMP	1 day	Tue 7/13/10	Tue 7/13/10	31	0%
33	Issue NTP & Mobilization	7 days	Wed 7/14/10	Thu 7/22/10	32	0%
34	Construction	190 days	Fri 7/23/10	Thu 4/14/11	33	0%
35	Prepare Bleacher Deferred Approval Submittal	20 days	Fri 8/6/10	Thu 9/2/10	34SS+10 d	0%
36	DSA Review of Bleacher Deferred Approval	100 days	Fri 9/3/10	Thu 1/20/11	35	0%
37	Bleacher Corrections & Sign-off	20 days	Fri 1/21/11	Thu 2/17/11	36	0%
38	Bleachers Installation	25 days	Fri 2/18/11	Thu 3/24/11	37	0%
39	Punch list & Close out	20 days	Fri 4/15/11	Thu 5/12/11	34	0%
40						
41	**Auditorium**	**634 days**	**Mon 12/8/08**	**Thu 5/12/11**		**67%**
42	User Group Meeting	0 days	Mon 12/8/08	Mon 12/8/08		100%
43	Public Meeting	0 days	Mon 12/15/08	Mon 12/15/08		100%
44	Master Planning	30 days	Mon 12/15/08	Fri 1/23/09	43	100%
45	Schematic Design	40 days	Tue 2/3/09	Mon 3/30/09	44	100%
46	SD Cost Estimate	14 days	Wed 4/15/09	Mon 5/4/09		100%
47	FAC Meeting: SD Presentation	0 days	Mon 3/30/09	Mon 3/30/09		100%
48	FAC Meeting: SD & Cost Estimate Presentation	0 days	Mon 5/4/09	Mon 5/4/09		100%
49	Design Development	54 days	Wed 4/1/09	Mon 6/15/09	45	100%
50	DD Cost Estimate	15 days	Tue 5/26/09	Mon 6/15/09		100%
51	FAC Board Meeting: Presentation of DD & Cost Estimate	0 days	Mon 6/22/09	Mon 6/22/09		100%
52	50% CD Set	22 days	Tue 6/23/09	Wed 7/22/09	51	100%
53	50% CD Cost Estimate	15 days	Thu 7/23/09	Wed 8/12/09	49	100%
54	100% CD Pricing Set	36 days	Fri 7/24/09	Fri 9/11/09	52	100%
55	100% CD Cost Estimate by CW Driver	18 days	Mon 9/14/09	Wed 10/7/09	54	100%
56	FAC Board Meeting to Review 100% CD estimate	0 days	Wed 10/7/09	Wed 10/7/09		100%
57	District & Board Review	5 days	Wed 10/7/09	Tue 10/13/09	56	100%
58	Incorporate District Comments	15 days	Wed 10/14/09	Tue 11/3/09	57	100%
59	Prepare DSA Submittal Package	5 days	Tue 11/3/09	Mon 11/9/09		100%
60	**DSA Submittal**	**0 days**	**Tue 11/10/09**	**Tue 11/10/09**	59	100%
61	DSA Review	100 days	Tue 11/10/09	Mon 3/29/10	60	100%
62	DSA Corrections & Resubmittal	47 days	Tue 3/30/10	Wed 6/2/10	61	100%
63	close out of previous DSA A#'s for Admin Bldg.	35 days	Thu 6/3/10	Wed 7/21/10	62	70%
64	**DSA Approval (estimated)**	**0 days**	**Wed 7/21/10**	**Wed 7/21/10**	63	0%
65	Bidding & Negotiation	39 days	Thu 7/22/10	Tue 9/14/10	64	0%
66	FAC Small Group meeting to review GMP	1 day	Wed 9/15/10	Wed 9/15/10	65	0%
67	FAC meeting to issue GMP Recommendation to BOE	1 day	Wed 9/22/10	Wed 9/22/10	66FS+4 da	0%
68	Board of Education Meeting to approve GMP	1 day	Tue 9/28/10	Tue 9/28/10	67FS+3 da	0%
69	Issue NTP & Mobilization	7 days	Wed 9/29/10	Thu 10/7/10	68	0%
70	Construction	135 days	Fri 10/8/10	Thu 4/14/11	69	0%
71	Punch list & Close out	20 days	Fri 4/15/11	Thu 5/12/11	70	0%
